






ROADSIDE CATCH BASIN PROTECTION DETAIL: TERRAFIX SILTSACK

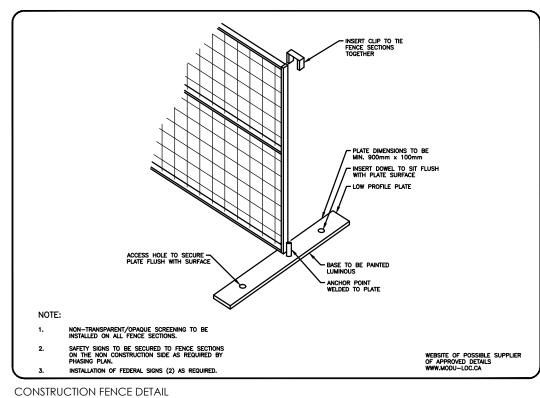


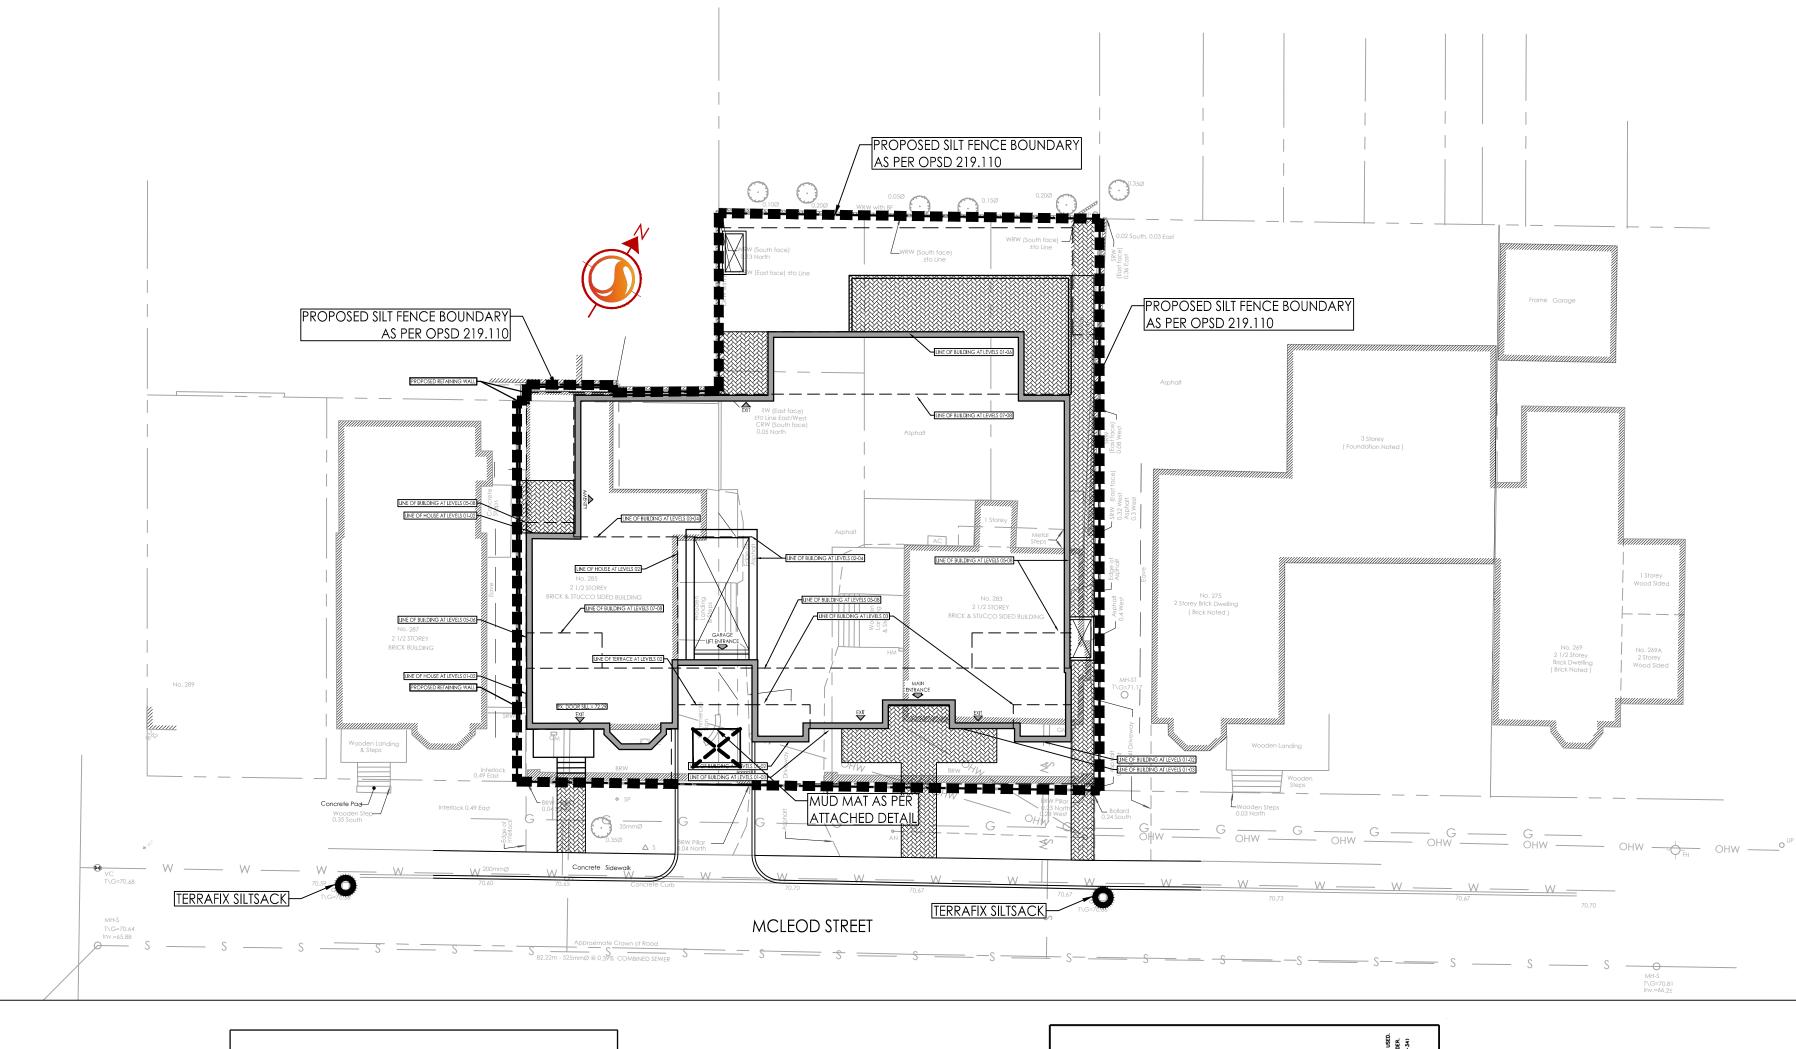

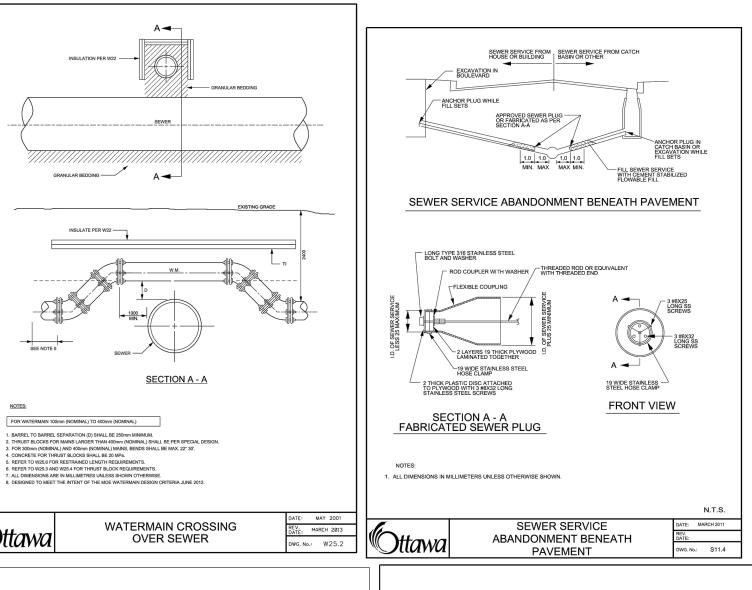

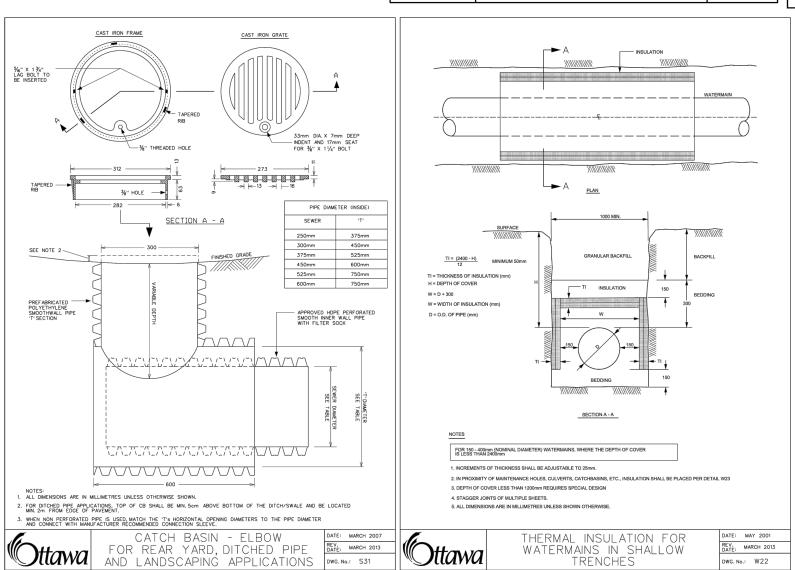

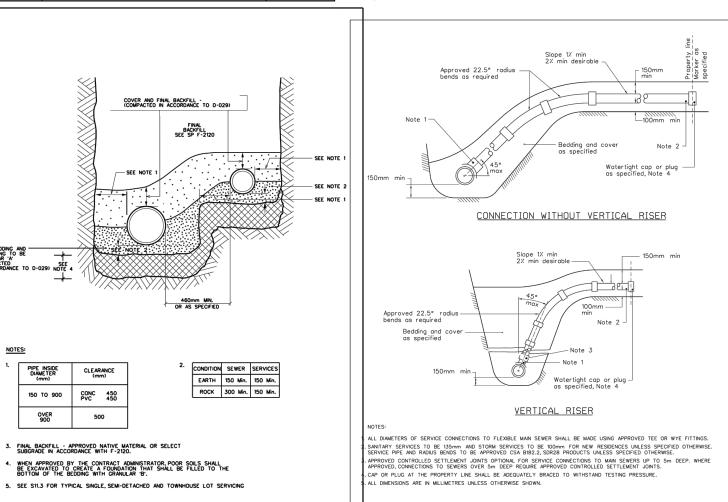

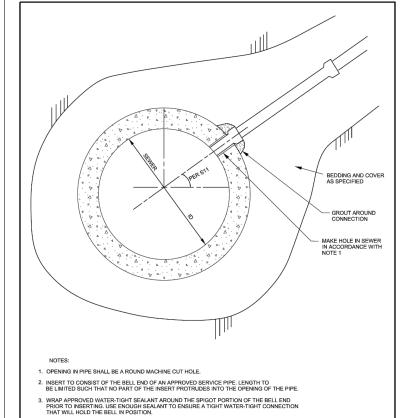

Stantec Consulting Ltd. 400 - 1331 Clyde Avenue Ottawa ON

Tel. 613.722.4420 www.stantec.com

Copyright Reserved

The Contractor shall verify and be responsible for all dimensions. DO NOT scale the drawing - any errors or omissions shall be reported to Stantec without delay The Copyrights to all designs and drawings are the property of Stantec. Reproduction or use for any purpose other than that authorized by Stantec is forbidden.

PROPOSED SILT FENCE BOUNDARY AS PER OPSD 219.110



PROPOSED CATCH BASIN PROTECTION AS PER DETAIL.



PROPOSED MUD MAT LOCATION



PROPOSED VALVE BOX PROPOSED VALVE CHAMBER PROPOSED FIRE HYDRANT

> PROPOSED SANITARY SEWER MANHOLE PROPOSED STORM SEWER MANHOLE PROPOSED CATCHBASIN

Notes

Best Management Practices

CONTRACTOR TO PROVIDE EROSION AND SEDIMENT CONTROLS (BEST MANAGEMENT PRACTICES) DURING CONSTRUCTION OF THIS PROJECT. THE CONTRACTOR SHALL IMPLEMENT BEST MANAGEMENT PRACTICES, TO PROVIDE FOR PROTECTION OF THE AREA DRAINAGE SYSTEM AND THE RECEIVING WATERCOURSE, DURING CONSTRUCTION ACTIVITIES. THE CONTRACTOR ACKNOWLEDGES THAT FAILURE TO IMPLEMENT APPROPRIATE EROSION AND SEDIMENT CONTROL MEASURES MAY BE SUBJECT TO PENALTIES IMPOSED BY ANY APPLICABLE REGULATORY AGENCY. EROSION MUST BE MINIMIZED AND SEDIMENTS MUST BE REMOVED FROM CONSTRUCTION SITE

RUN-OFF IN ORDER TO PROTECT DOWNSTREAM AREAS. DURING ALL CONSTRUCTION, EROSION AND

1. LIMIT THE EXTENT OF EXPOSED SOILS AT ANY GIVEN TIME.

SEDIMENTATION SHOULD BE CONTROLLED BY THE FOLLOWING TECHNIQUES:

- REVEGETATE EXPOSED AREAS AND SLOPES AS SOON AS POSSIBLE.

CONTRACTOR WITHOUT DELAY.

- MINIMIZE AREA TO BE CLEARED AND GRUBBED.
- PROTECT EXPOSED SLOPES WITH PLASTIC OR SYNTHETIC MULCHES.
- INSTALL CATCH BASIN INSERTS OR EQUIVALENT IN ALL PROPOSED CATCH BASINS AND CATCH BASIN MANHOLES AND IN ALL EXISTING CATCH BASINS THAT WILL RECEIVE RUN-OFF FROM THE
- A SILT FENCE SHALL BE INSTALLED AROUND THE PERIMETER OF ALL AND ANY STOCKPILES OF MATERIAL TO BE USED OR REMOVED FROM SITE. (LOCATION TO BE DETERMINED)
- A VISUAL INSPECTION SHALL BE DONE DAILY ON SEDIMENT CONTROL MEASURES AND CLEANED OF ANY ACCUMULATED SILT AS REQUIRED. THE DEPOSITS WILL BE DISPOSED OFF
- SITE AS PER THE REQUIREMENTS OF THE CONTRACT. SEDIMENT CONTROL BARRIERS MAY ONLY BE REMOVED TEMPORARILY WITH APPROVAL OF CONTRACT ADMINISTRATOR TO ACCOMMODATE CONSTRUCTION OPERATIONS. ALL AFFECTED
- BARRIERS MUST BE REINSTATED AT NIGHT WHEN CONSTRUCTION IS COMPLETED. NO REMOVAL WILL OCCUR IF THERE IS A SIGNIFICANT RAINFALL EVENT ANTICIPATED (>10mm) UNLESS A NEW DEVICE HAS BEEN INSTALLED TO PROTECT EXISTING STORM AND SANITARY SEWER SYSTEMS, OR DOWNSTREAM WATERCOURSES. NO REFUELING OR CLEANING OF EQUIPMENT IS PERMITTED NEAR ANY EXISTING WATERWAY.

CONTRACTOR SHALL REMOVE SEDIMENT CONTROL MEASURES WHEN, IN THE OPINION OF THE CONTRACT ADMINISTRATOR, THE MEASURE(S) IS NO LONGER REQUIRED. NO CONTROL

- MEASURES SHALL BE PERMANENTLEY REMOVED WITHOUT PRIOR WRITTEN AUTHORIZATION FROM THE CONTRACT ADMINISTRATOR. THE CONTRACTOR SHALL PERIODICALLY, OR WHEN REQUESTED BY THE CONTRACT
- ADMINISTRATOR, CLEAN OUT ACCUMULATED SEDIMENTS AS REQUIRED. THE CONTRACTOR SHALL IMMEDIATELY REPORT TO THE ENGINEER ANY ACCIDENTAL DISCHARGES OF SEDIMENT MATERIAL INTO THE WATERCOURSE, APPROPRIATE RESPONSE MEASURES, INCLUDING ANY REPAIRS TO EXISTING CONTROL MEASURES OR THE IMPLEMENTATION OF ADDITIONAL CONTROL MEASURES, SHALL BE CARRIED OUT BY THE
- 13. CONTRACTOR SHALL INSTALL MUD MATS AT ALL CONSTRUCTION ENTRANCES TO THE SITE.
- 14. STORMWATER SWALES TO BE COVERED WITH HYDRO-SEED AND MULCH.

2 ISSUED FOR APPROVAL		AJ	ALG	21.08.13
1 ISSUED FOR REVIEW		AJ	ALG	21.08.06
Revision		Ву	Appd.	YY.MM.DD
File Name: 160401560-DB	AJ	ALG	AJ	21.08.01

Dwn. Chkd. Dsgn. YY.MM.DD

Permit-Seal



Client/Project

CENTRETOWN 283-285 McLEOD STREET OTTAWA, ON, CANADA

ZYER DEVELOPMENTS

EROSION CONTROL AND **DETAIL SHEET**

Project No. 160401560 Drawing No. Revision

ORIGINAL SHEET - ARCH D

150 TO 900 CONC 450 PVC 450 OVER 900 500 FINAL BACKFILL - APPROVED NATIVE MATERIAL OR SELECT SUBGRADE IN ACCORDANCE WITH F-2120. 4. WHEN APPROVED BY THE CONTRACT ADMINISTRATOR, POOR SOILS SHALL BE EXCAVATED TO CREATE A FOUNDATION THAT SHALL BE FILLED TO THE BOTTOM OF THE BEDDING WITH GRANULAR 'B'. 5. SEE S11.3 FOR TYPICAL SINGLE, SEMI-DETACHED AND TOWNHOUSE LOT SERVICING

COMBINED TRENCH

(SEWERS & SEWER SERVICES)

SEWER SERVICE CONNECTIONS
FOR FLEXIBLE MAIN SEWER PIPE REV. DATE: MARCH 2013

STANDARD TRENCH REINSTATMENT

IN PAVED SURFACE

4. GROUT AROUND THE BELL END TO PROTECT THE SEALANT AND SUPPORT THE BELL. ALL OTHER NOTES OF S11 APPLY. 6. SEE MS-22.15 FOR APPROVED SEALANT PRODUCTS.

SEWER SERVICE CONNECTIONS

FOR RIGID MAIN SEWER PIPE USING BELL END INSERT METHOD

PLAN #
